

Completed Activities

- Project Reports & Environmental Documents
 Approved for Eastbound and Westbound
- Civil Design Complete for Eastbound and Westbound as a one contract
- Completed Preliminary Design Document (PDD) for Electronic Toll System
- Issued Tier 2 and 3 CCOs to Contractors

ommittee – June 2014



2

Ongoing Activities

- Working on Electronic Toll System Design
- Developing Public Outreach/Education Plan
- Preparing various Agreements

I-580 Policy Committee – June 2014



Upcoming Activities

- Begin Public Outreach Campaign in May/June 2014
- Complete Detailed Design Document (DDD) for Electronic Toll System by August 2014
- Develop, Negotiate & Process Various Agreements
- Process Contract Amendments with URS for Additional Design Services and Design Support During Construction
- Develop & Process CCOs with ETCC for Items Related to Vehicle Enforcement System

I-580 Policy Committee – June 2014




4

Continuous Access Implementation

Key Elements Under Development

- · Electronic Toll System Design
 - Automated Violation Enforcement
 - Business Rules
- Toll Ordinance
- Legislation
- Agency Agreements
- · Public Outreach/Education Plan Im








.

Express Lane Schedule Environmental Document & Project Report Approval (Westbound) Environmental Document & Project Report Approval (Eastbound) Design Tier I Contract Change Order Work Civil Construction

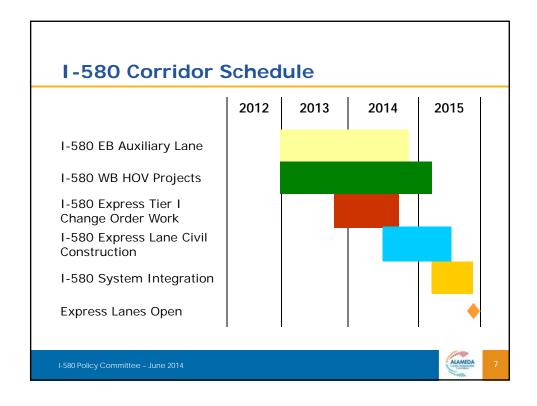

I-580 Express Lane Funding Project Phase Funding Source (\$ x million) ARRA TVTC **TCRP** Federal RM2 Local Total Deferred (Meas. B) Earmark PA&ED 1.39 2.17 0.10 3.66 PS&E 0.70 0.11 0.93 4.84 3.10 Sys. Int. 6.80 1.47 8.05 17.00 0.68 ROW 0.37 0.37 2.55 0.05 1.47 4.07 Const. Support Construct Cap 1.00 24.56 0.63 1.28 21.65 O&M 0.48 0.48 TOTAL 7.50 1.00 31.65 54.98 4.78 6.0 4.05 Total Project Cost: \$54.98 M
