




I-680 NB Express Lane Monthly Project Status Update

A Presentation for the
Sunol Smart Carpool Lane Joint Powers Authority (SSCLJPA)
June 09, 2014




Progress Reporting

- ▣ Activities Completed
- ▣ Upcoming PA&ED Activities



I-680 Sunol SMART Carpool Lane Joint Powers Authority



2

Activities Completed

- ❑ Environmental Technical Studies, Reports, Traffic Reports and Engineering Reports
- ❑ Stakeholder/Public Participation
Project Development Team meeting (on-going)

Upcoming PA&ED Activities in 2014


- ❑ Project Approval
 - ✓ Draft Project Report (August 2014)
- ❑ Environmental Document
 - ✓ Draft EIR/EA (August 2014)
 - ✓ Public Circulation of Draft EIR/EA (August – September 2014)
 - ✓ Public Hearing (September 2014)

Key Focus Areas

- ❑ Funding
- ❑ Project Phasing
- ❑ Implementation of a Financially Constrained Alternative
- ❑ Schedule

Traffic Study Limits & Approach

- ❑ Study Envelope
- ❑ Local Approval on Study Approach

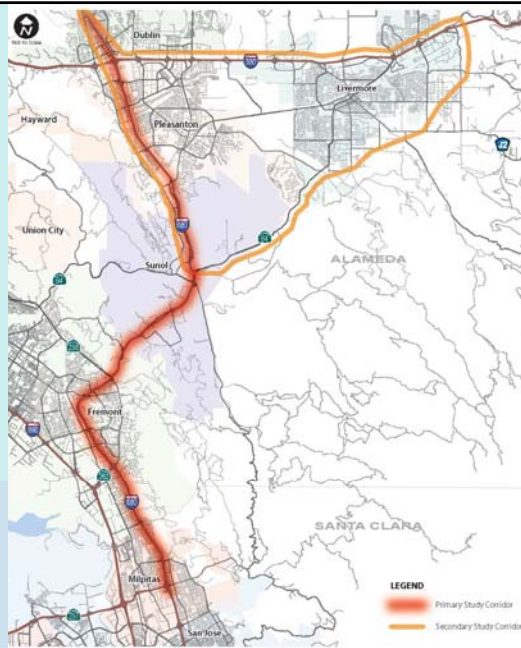

Project Schedule	
Project Initiation Document (PID)	October 2012 (A)
Project Approval (PA&ED)	July 2015 (T)
Ready to List (PS&E)*	March 2017 (T)
Right of Way Cert.*	March 2017 (T)
Begin Construction*	July 2017 (T)
End Construction (CCA)*	December 2018 (T)
* Subject to funding availability	

I-680 Sunol SMART Carpool Lane Joint Powers Authority  7
