


<section-header><section-header><section-header><section-header><list-item><list-item><list-item><list-item><list-item><list-item><list-item><list-item><list-item>




Prop 1B Bond Projects Cost/Funding

Project Description	Total Project Cost	Total Bond Funds	Bond Type
1. I-580 Eastbound HOV Lane (Segments 1, 2 & 3 – AUX Lanes)	\$137.2	\$55.2	CMIA
2. I-580 Westbound HOV Lane (East & West Segments)	\$143.9	\$82.4	CMIA
3. Isabel Ave., I-580 / Route 84 Interchange	\$111.7	\$45.3	CMIA
4. I-880 Southbound HOV Lane (North & South Segments)	\$106.5	\$82.6	CMIA
5. I-80 ICM (Sub-projects 1-6)	\$80.0	\$66.2	CMIA, TLSF
6. Route 84 Expressway (North & South Segments)	\$122.0	\$16.1	CMIA
7. I-880 North Safety and Operational Improvements at 23 rd /29 th Avenues	\$99.9	\$73.4	TCIF
Total:	\$801.2	\$421.2*	
* Total reflects bid savings to date			
Prop. 1B Bond Program Update	September 2013		ALAMEDA

Project	Begin Construction (See Note)	End Construction (See Note)		
1 I-580 Eastbound HOV Segment 1&2	Projects Complete			
I-580 Eastbound HOV Segment 3 with AUX Lane	NOV 2012 (A)	NOV 2014 (T		
2 I-580 Westbound HOV – East Segment	NOV 2012 (A)	NOV 2014 (T		
I-580 Westbound HOV – West Segment	OCT 2012 (A)	NOV 2014 (T		
3 Isabel Ave., I-580 / Route 84 Interchange	Project Comple	Project Complete		
4 I-880 Southbound HOV – North Segment	NOV 2012 (A)	JUL 2015 (T)		
I-880 Southbound HOV – South Segment	SEP 2012 (A)	MAY 2015 (T)		
5 I-80 Integrated Corridor Mobility (ICM)	JUN 2011 (A)	DEC 2014 (T)		
6 Route 84 Expressway – North Segment	MAR 2012 (A)	FEB 2014 (T)		
7 I-880 Operational Improvements at 23 rd /29 th Avenues	DEC 2013 (T)	DEC 2017 (T)		
Note: (A)=Actual (T)=Target Construction start dates contingent upon winter weat	her conditions			
Prop. 18 Bond Program Update	September 2013	ALAMEDA		

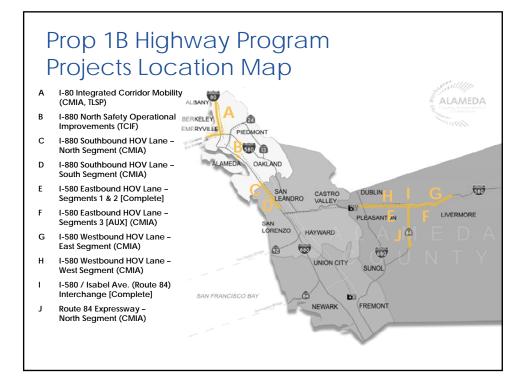


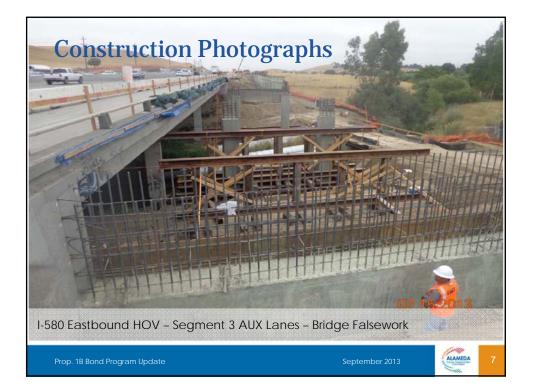







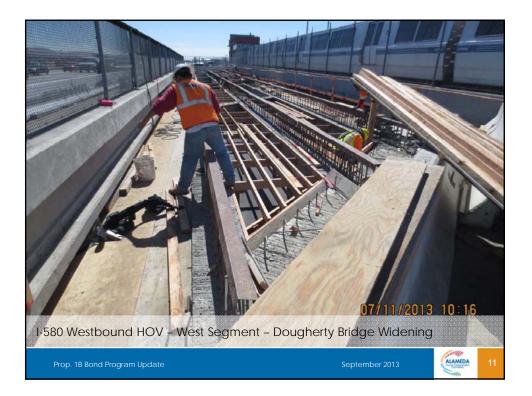





This page intentionally left blank.
